


ID	Health	Task Mode	Task Name	Duration	Predecessors	Successors	Half 2, 2025							Half 1, 2026					Half 2, 2026					Half 1, 2027					Half 2, 2027					Half 1, 2028					Half
							S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	
1	🔴	➡	Ethandakukhanya CHC - Project Schedule to Completion	240 days			[Timeline bar from start to end]																																
2	🔴	➡	Key Milestones	240 days			[Timeline bar from start to end]																																
3	🔴	➡	Appointment of Replacement Contractor	0 days	9		[Timeline bar from start to end]																																
4	🔴	➡	Site Handover	0 days	13		[Timeline bar from start to end]																																
5	🔴	➡	Practical Completion	0 days	86		[Timeline bar from start to end]																																
6	🔴	➡	Health Technology Equipping	0 days	113		[Timeline bar from start to end]																																
7	🔴	➡	Final Completion	0 days	130		[Timeline bar from start to end]																																
8	🔴	➡	Procurement of Completion Contractor	20 days			[Timeline bar from start to end]																																
9	🔴	➡	Procurment Gate 7: Tender Award	0 days		10,3,11	[Timeline bar from start to end]																																
10	🔴	➡	Procurment Gate 8: Ensure Compliance	20 days	9	14	[Timeline bar from start to end]																																
11	🔴	➡	Application for the Construction Works Permit	20 days	9	13	[Timeline bar from start to end]																																
12	🔴	➡	Commencement with Remaining Works	148 days			[Timeline bar from start to end]																																
13	🔴	➡	Site Handover to New Contractor	1 day	11	4,14	[Timeline bar from start to end]																																
14	🔴	➡	Commencement of Works	7 days	13,10	18,16,20,17,74	[Timeline bar from start to end]																																
15	🔴	➡	Block A - MOU (Maternity)	15 days		45,51,88	[Timeline bar from start to end]																																
16	🔴	➡	Install HVAC Units and Control Panels to Walls	15 days	14	22	[Timeline bar from start to end]																																
17	🔴	➡	Completion of Cold Room Works	10 days	14	82	[Timeline bar from start to end]																																
18	🔴	➡	Fire Detection, CCTV and Access Control Wiring	10 days	14	19	[Timeline bar from start to end]																																
19	🔴	➡	Install Final Fixes Fire Detection, CCTV and Access Control	4 days	18	23	[Timeline bar from start to end]																																
20	🔴	➡	Install Medical Gas	4 days	14	24	[Timeline bar from start to end]																																
21	🔴	➡	Block B – Minor Ailments	26 days			[Timeline bar from start to end]																																
22	🔴	➡	Install HVAC Units and Control Panels to Walls	15 days	16	26	[Timeline bar from start to end]																																
23	🔴	➡	Install Final Fixes Fire Detection, CCTV and Access Control	4 days	19	27	[Timeline bar from start to end]																																
24	🔴	➡	Install Medical Gas	4 days	20	28	[Timeline bar from start to end]																																
25	🔴	➡	Block C – Equipment Store, Ablutions, Courtyard	32 days			[Timeline bar from start to end]																																
26	🔴	➡	Install HVAC Units and Control Panels to Walls	10 days	22	30	[Timeline bar from start to end]																																
27	🔴	➡	Install Final Fixes Fire Detection, CCTV and Access Control	4 days	23	31	[Timeline bar from start to end]																																
28	🔴	➡	Install Medical Gas	4 days	24	33	[Timeline bar from start to end]																																
29	🔴	➡	Block D – Emergency Services	38 days			[Timeline bar from start to end]																																
30	🔴	➡	Install HVAC Units and Control Panels to Walls	10 days	26	35	[Timeline bar from start to end]																																
31	🔴	➡	Install Final Fixes Fire Detection, CCTV and Access Control	4 days	27	36,32	[Timeline bar from start to end]																																
32	🔴	➡	Installation of Nurses Call	4 days	31	36	[Timeline bar from start to end]																																
33	🔴	➡	Install Medical Gas	4 days	28	44	[Timeline bar from start to end]																																
34	🔴	➡	Block E – Central Waiting Area	30 days			[Timeline bar from start to end]																																
35	🔴	➡	Install HVAC Units and Control Panels to Walls	10 days	30	38	[Timeline bar from start to end]																																
36	🔴	➡	Install Final Fixes Fire Detection, CCTV and Access Control	4 days	31,32	39	[Timeline bar from start to end]																																
37	🔴	➡	Block F – Reception	36 days			[Timeline bar from start to end]																																
38	🔴	➡	Install HVAC Units and Control Panels to Walls	10 days	35	41	[Timeline bar from start to end]																																
39	🔴	➡	Install Final Fixes Fire Detection, CCTV and Access Control	4 days	36	42	[Timeline bar from start to end]																																
40	🔴	➡	Block G – Health Support Services	65 days			[Timeline bar from start to end]																																
41	🔴	➡	Install HVAC Units and Control Panels to Walls	10 days	38	47	[Timeline bar from start to end]																																
42	🔴	➡	Install Final Fixes Fire Detection, CCTV and Access Control	4 days	39	43	[Timeline bar from start to end]																																
43	🔴	➡	Fire Detection, CCTV and Access Control Wiring	10 days	42	49	[Timeline bar from start to end]																																
44	🔴	➡	Install Medical Gas	4 days	33	65	[Timeline bar from start to end]																																
45	🔴	➡	Installation of Dental Chairs and X-Ray Equipment	10 days	15		[Timeline bar from start to end]																																
46	🔴	➡	Block H – Chronic Care	85 days			[Timeline bar from start to end]																																
47	🔴	➡	Install HVAC Units and Control Panels to Walls	10 days	41	48,53	[Timeline bar from start to end]																																
48	🔴	➡	Install HVAC Louvres and Air Vents	10 days	47		[Timeline bar from start to end]																																
49	🔴	➡	Fire Detection, CCTV and Access Control Wiring	15 days	43	50	[Timeline bar from start to end]																																
50	🔴	➡	Install Final Fixes Fire Detection, CCTV and Access Control	5 days	49	58	[Timeline bar from start to end]																																
51	🔴	➡	Install Joinery Cupboards and Shelving	10 days	15		[Timeline bar from start to end]																																
52	🔴	➡	Block I – Courtyard, Surgical Store, Community Outreach, Public	10 days			[Timeline bar from start to end]																																



Project: Ethandakukhanya CHC Date: 15 May 2026	Task		Inactive Task		Manual Summary Rollup		External Milestone		Baseline Milestone	
	Split		Inactive Milestone		Manual Summary		Deadline		Baseline Summary	
	Milestone		Inactive Summary		Start-only		Critical		Progress	
	Summary		Manual Task		Finish-only		Critical Split		Manual Progress	
	Project Summary		Duration-only		External Tasks		Baseline			



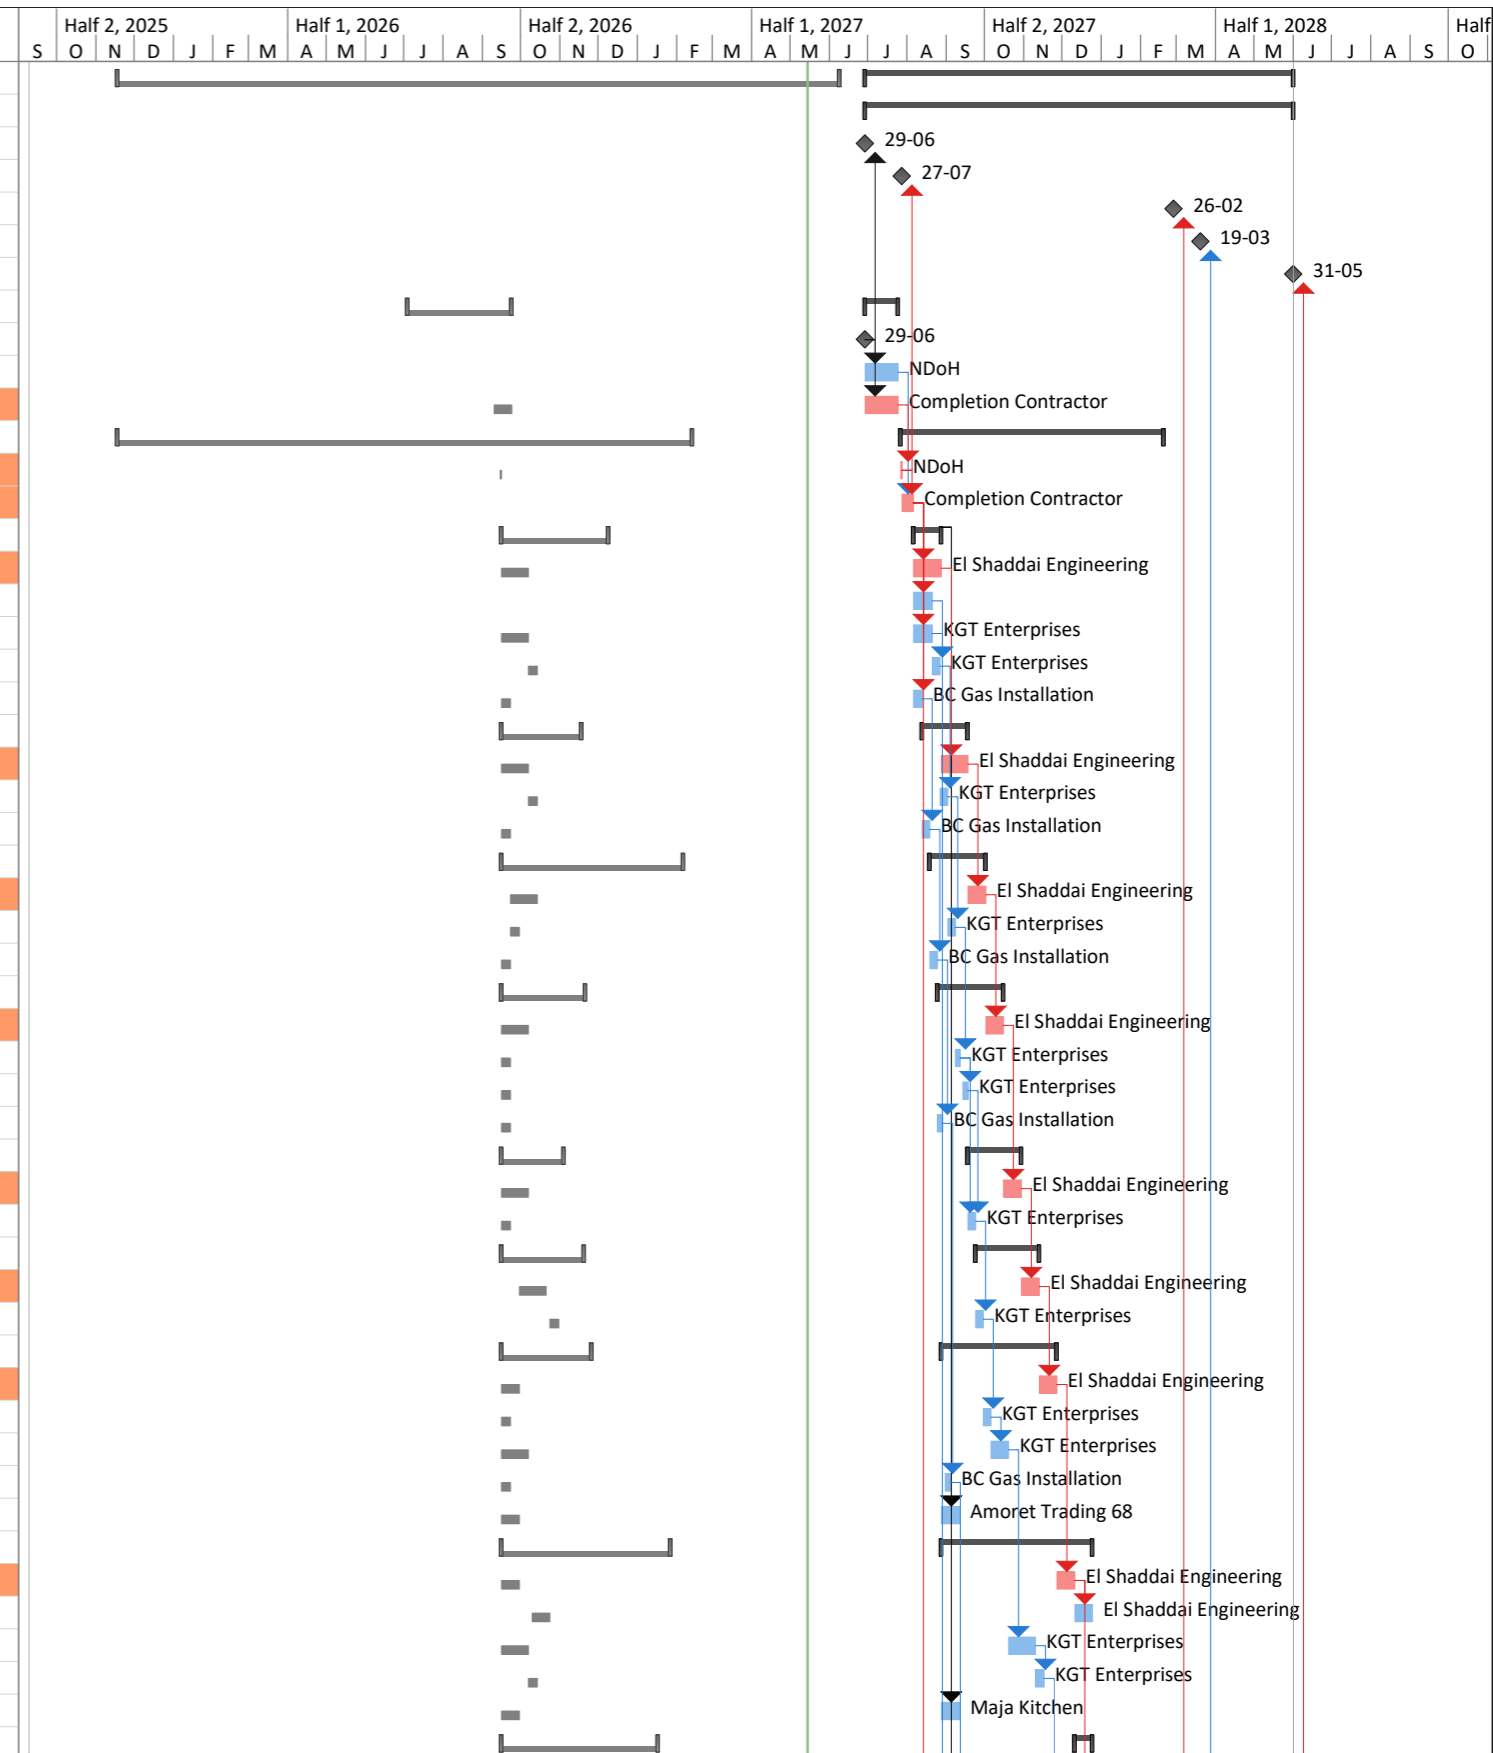
